

Planning & Roadmap

Smart Metering & Consumption Intelligence Platform
Q3 2026

Q3 – 2026 Plan – Meter Reading Ingestion & Billing Engine

13 Weeks • 6 Sprints • 4 Phases

Phased Approach — Build Bottom,Up

Phase 1: Foundation (Weeks 1,4)

Data model (6 entities) & ingestion pipeline
Validation, duplicate check, seed data

Phase 2: Business Logic (Weeks 5,8)

Tariff lookup (time,aligned) & cost calculation
Billing batch, prepaid/postpaid, lifecycle

Phase 3: Intelligence (Weeks 9,12)

Late arrival detection & anomalies
Alerting, dashboards, dispute workflow

Phase 4: Hardening (Week 13)

Integration test, performance test (18 Million rows)
UAT, go, live deploy, rollback plan

Why This Order? — MoSCoW Prioritisation

P1 Must Have

Data model & schema, Foundation, everything depends on this

P2 Must Have

Ingestion pipeline, No data = no billing = no revenue


P3 Must Have

Tariff & billing engine, Core revenue function

P4 Should Have

Detection & alerting, Quality layer, can go live without it

Roadmap Timeline — Visual

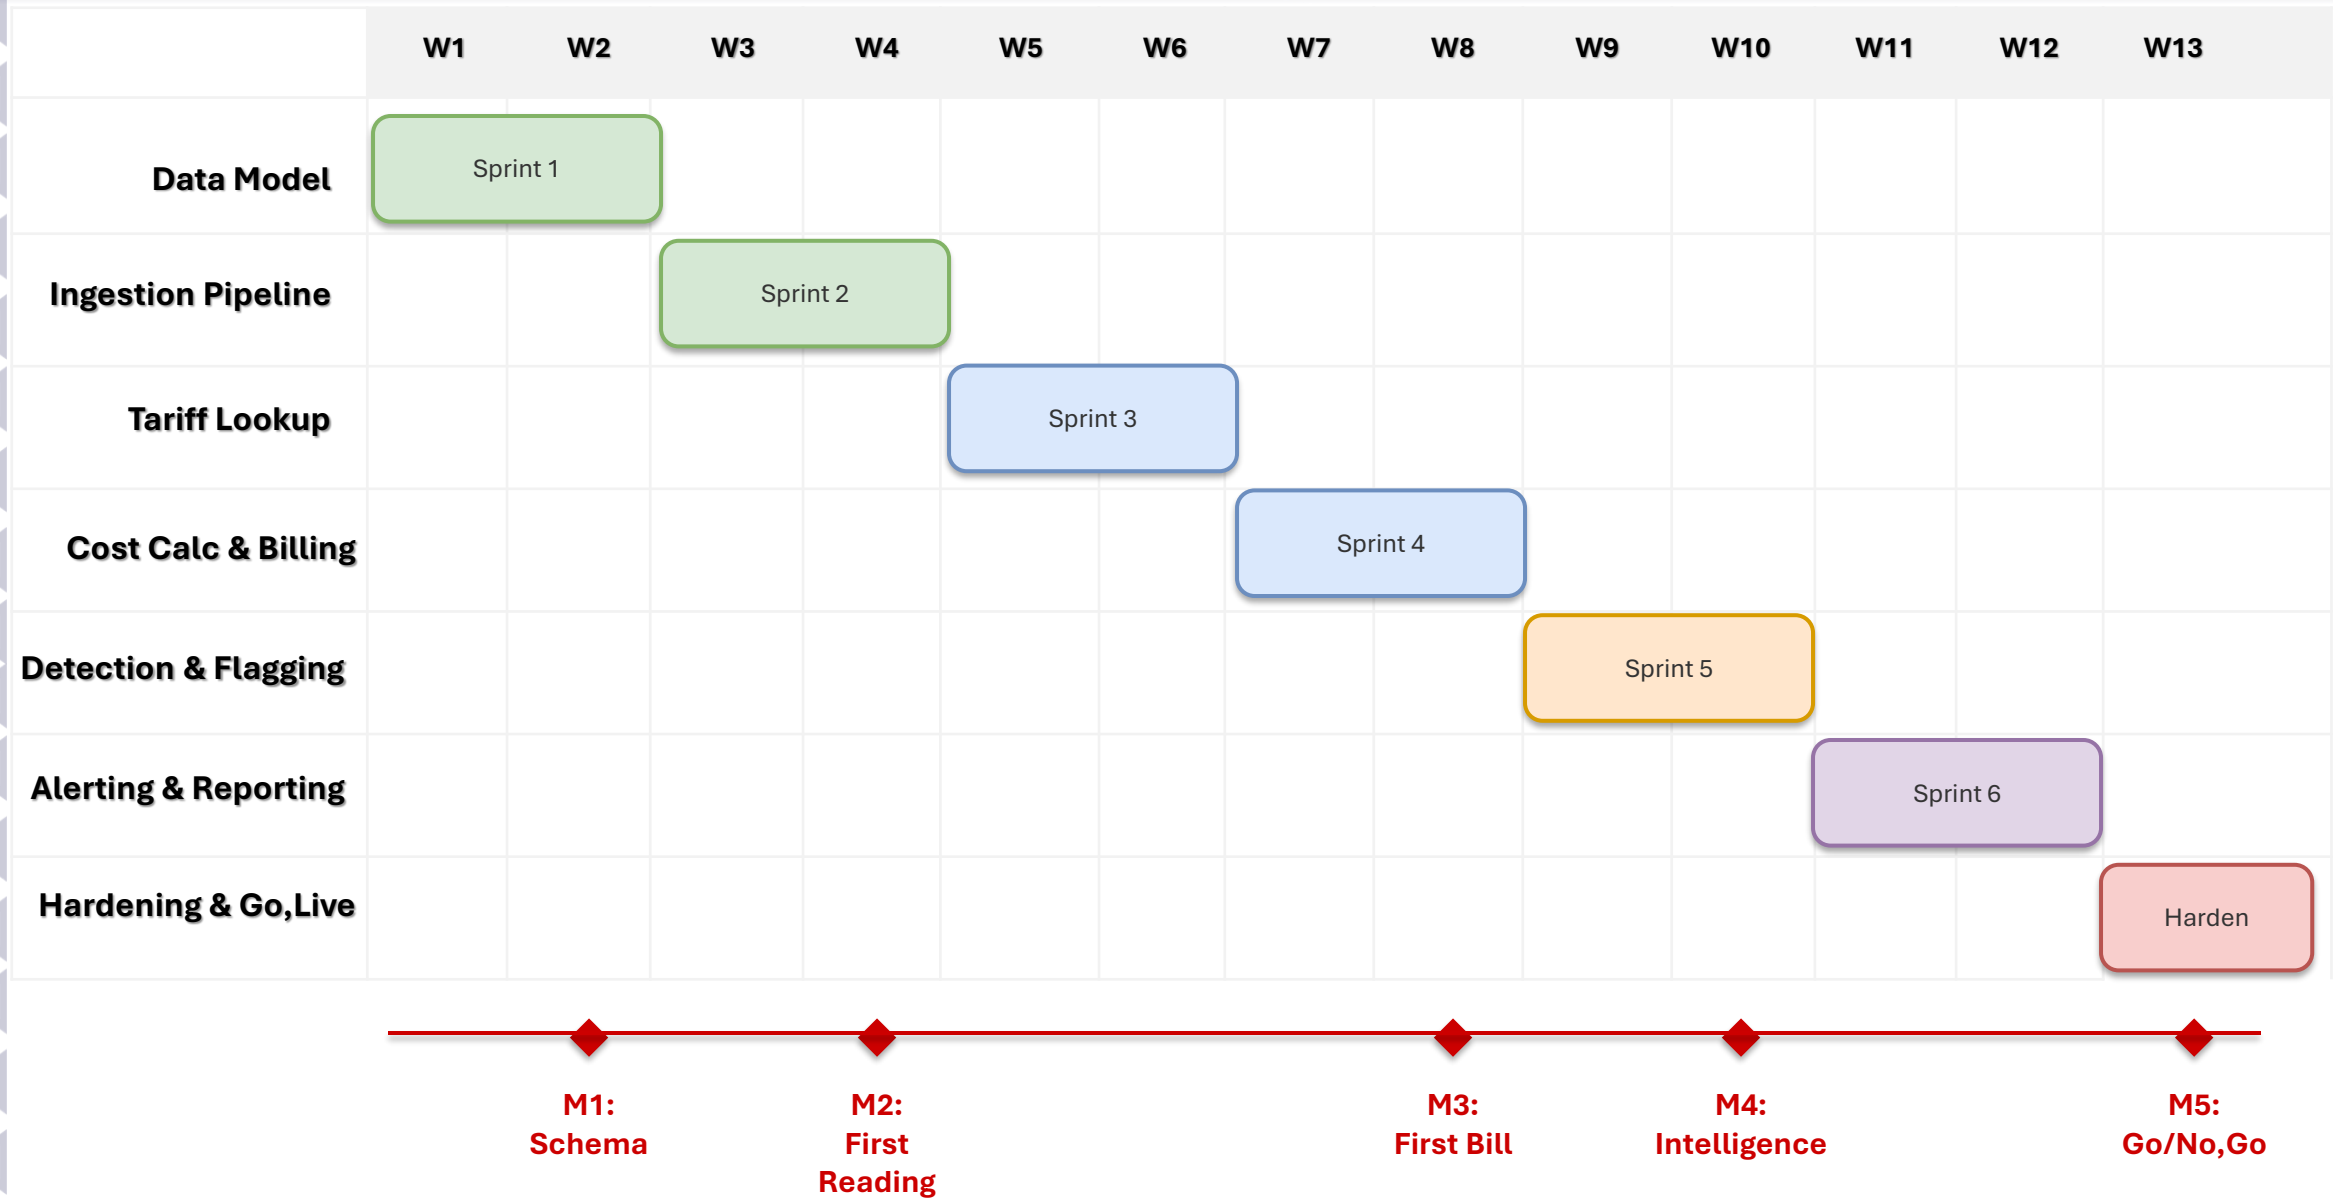

Dependencies, Risks & Success Metrics



Dependencies & Risks



Smart meter feed available by Week 3



DB environments provisioned by Day 1



Tariff config from business by Week 1



Message queue (Kafka) by Week 3



Alerting service by Week 11

Risk	Likelihood	Impact	Mitigation
Meter feed delayed	Med	High	Simulated data; defer integration
Tariff edge cases	High	Med	Sprint 3 dedicated; business in testing
Performance at scale	Med	High	Test 18M rows early; tune indexes
Scope creep	High	Med	Strict MoSCoW; defer to Q4



Success Metrics

Metric	Target	Measurement
Ingestion success	> 99.5%	Valid / total received
Duplicate rejection	100%	Zero duplicates in READINGS
Tariff match rate	> 99%	Readings with price / validated
Billing accuracy	100%	Matches manual spot, checks
Late arrival detection	100%	All >24hr flagged
Query performance	< 5 sec	All 4 queries within SLA
